METAL BLOCK | Order Form

MAC
METAL ARCHITECTURAL

CUSTOMER INFORMATION

Name : _____ Client Ref. No. : _____ Phone : _____

Responsable : _____ Email : _____

Address : _____ Project Name : _____

_____

Metal Block Profile

Gauge : Color :

Please fill in the following lines clearly indicating your needs :

A = Corresponds to the total length of the panel

B = Corresponds to the distance between the grooves (only if other than the standard which is every 24")

C = Corresponds to the measurement of the first groove starting from the right side of the panel


S clips (M16G) = When ordering S clips (M16G), you must confirm if the panel needs to be notched at the ends.
An additional charge of $0.10 per square foot will be applied. Indicate an **«N»** next to the panels quantity for those to be added.

IMPORTANT NOTES :

→ **NOTCHE**
- The panels cannot be notched if the measurements B and C are not identical.

→ **GROOVES**
- Distance can be from 12 in to 42 in. A minimum interval of 12 inches between grooves.
- 1st groove needs to be placed at a minimum of 6 in from the edge

→ **MANUFACTURING TOLERANCE**
- The groove positioning on the Metal Block profile may vary by up to ± 1/8 in. from the specified dimensions. This manufacturing tolerance may result in a slight offset on either side.

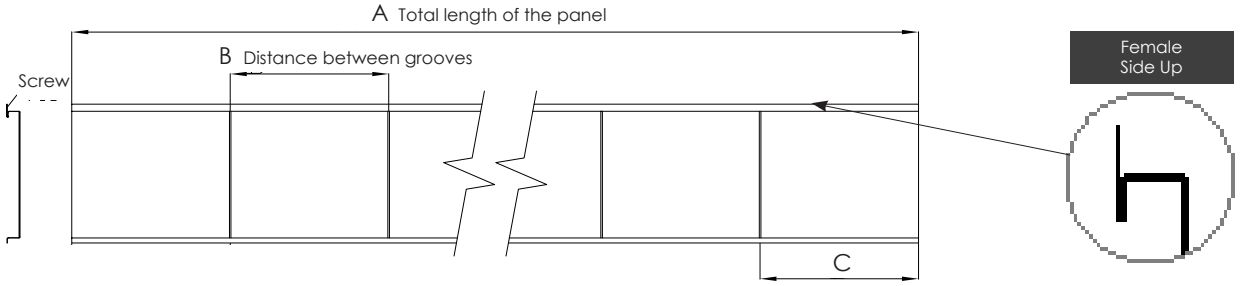

Plank Number	Plank Quantity	**"A"** Plank Length	**"B"** Distance between the grooves	**"C"** Distance of the 1st groove from the right (min. of 6 in)
Plank 1				
Plank 2				
Plank 3				
Plank 4				
Plank 5				
Plank 6				
Plank 7				
Plank 8				
Plank 9				
Plank 10				

MAC Metal Architectural
5975 Ch. de la Savane,Saint-Hubert, QC J3Y 0X1 | T. 450-464-5486 F. 450-464-4538

METAL BLOCK | Order Form


MAC
METAL ARCHITECTURAL

ADD RIGIDITY TO THE ENDS OF THE PANEL

It is strongly recommended to add rigidity brackets (ABRA3) on both ends of the panel.

In the event of panel bowing, MAC recommends installing ABRA4 U-shaped reinforcement brackets 6 inches from the ends of the panel.

For vertical installation, MAC strongly recommends the use of a ventilated J-trim (M01VG) at the bottom of the panel. Refer to the installation guide for more details on this installation.

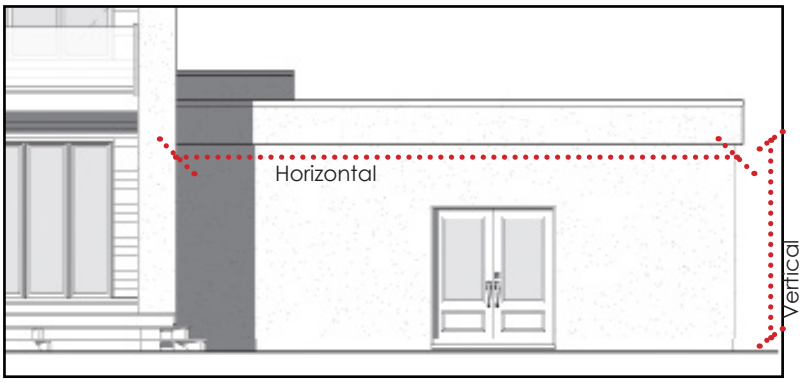

Plank Number	Plank Quantity	**"A"** Plank Length	**"B"** Distance between the grooves	**"C"** Distance of the 1st groove from the right (min. of 6 in)
Plank 11				
Plank 12				
Plank 13				
Plank 14				
Plank 15				
Plank 16				
Plank 17				
Plank 18				
Plank 19				
Plank 20				
Plank 21				
Plank 22				
Plank 23				
Plank 24				
Plank 25				
Plank 26				
Plank 27				
Plank 28				
Plank 29				
Plank 30				

Special Comment :
